




**HUNT MIDWEST**  
**RESIDENTIAL DEVELOPMENT**

# 76<sup>th</sup> St. Sidewalk Project Progress Update

4-20-11

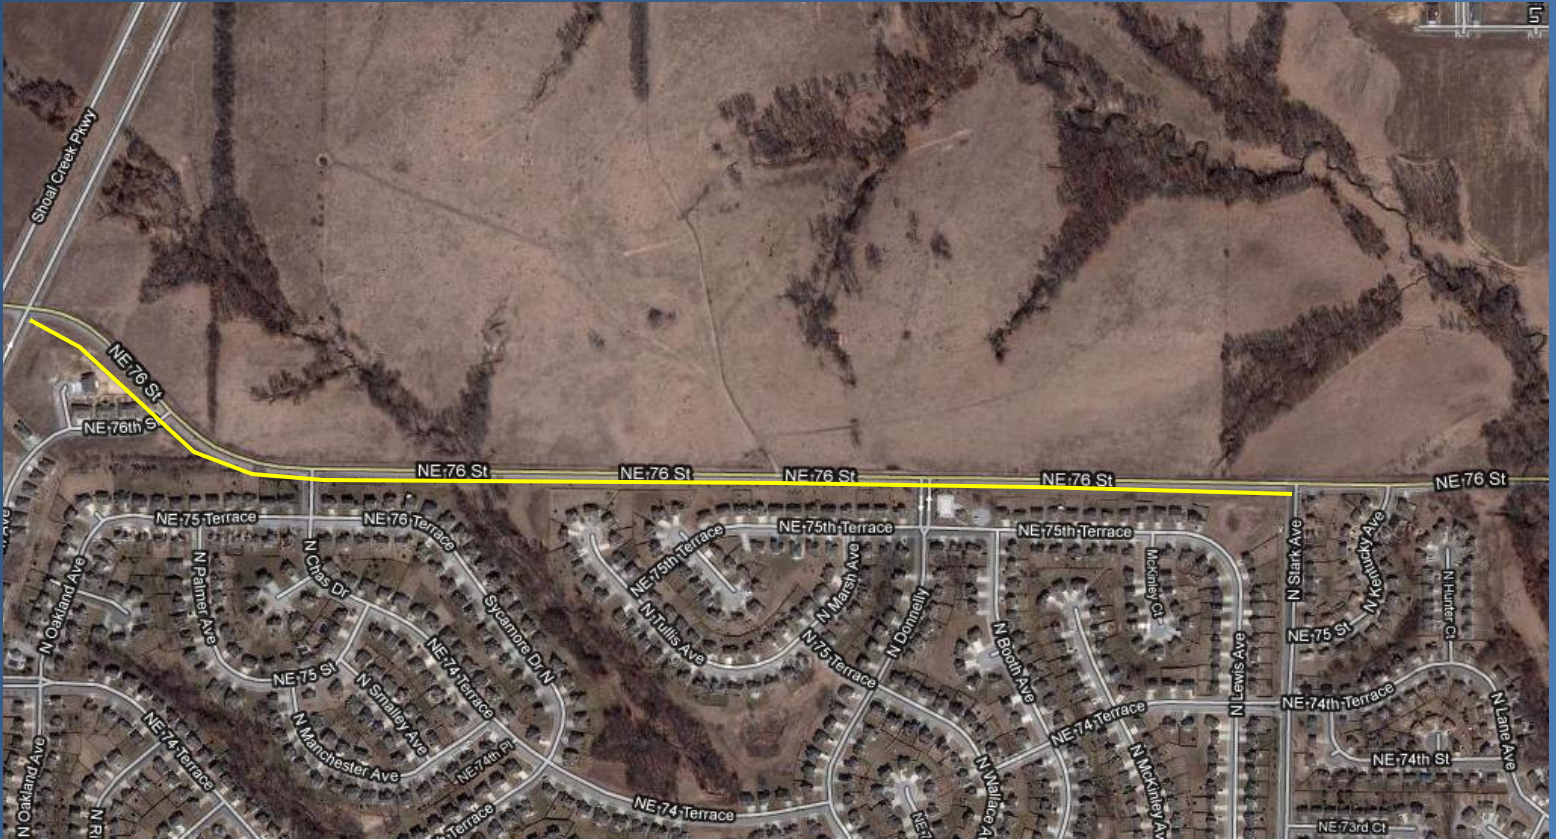

**Project Information** – 76<sup>th</sup> St. sidewalk is a 5' section of sidewalk that will run from Shoal Creek Parkway to N. Stark Avenue on the South side of 76<sup>th</sup> Street.

**Design** – The design is 100% complete and we are ready for construction when the permits are released.

**Construction** – Construction is scheduled to begin in early spring of 2011. The following are the main construction items and their percentage of completion. Construction items are in chronological order.

Grading – 90% complete  
Concrete – 45% complete  
Landscaping – 0% complete

**Improvement completion – early summer 2011 pending good weather.**
